



# Topics Addressed

ESSER III Project Updates

Scheduling

Budget Updates





# Jim Hill

## **Project Scope**

Indoor Air Quality Upgrades  
2 Pipe to 4 Pipe Conversion  
New Chillers, Boilers, and




# Bailey APAC

**Architect: Eley Guild Hardy**  
**Contractor: Alliant Construction**  
**Contract Amount: \$17,372,000**  
**Number of Contract Days: 435**  
**Number of Days into Construction: 168**


## Project Scope

HVAC/Indoor Air Quality Upgrades  
Classroom Reconfiguration (Ground Floor)  
New Ceilings & Lighting in Corridors  
Restroom Renovations  
Roof Replacement  
Drainage Repairs

## Construction Completion

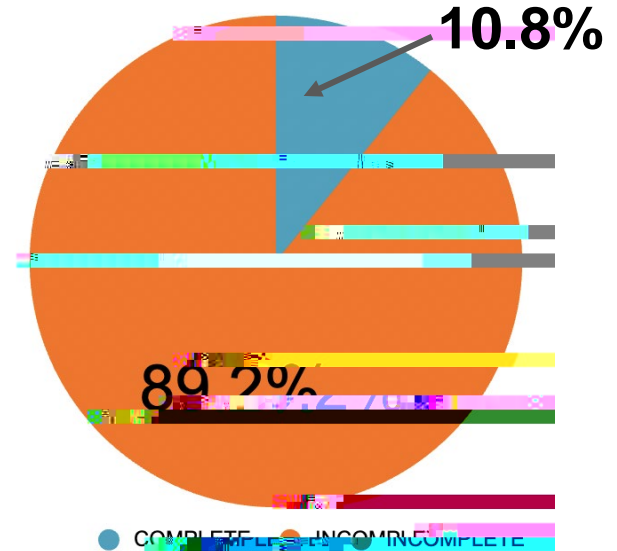

Sprinkler Heads Installed in Gym

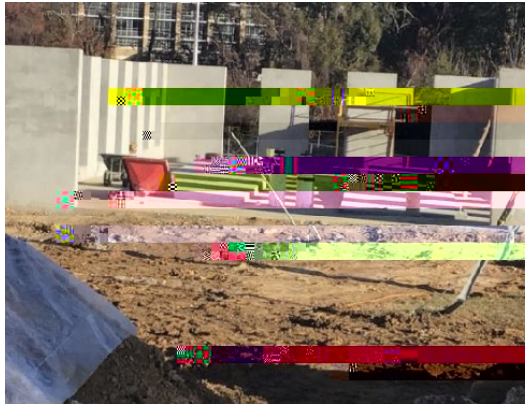

Concrete Pad for Chiller Installation

**Contract Completion Date:**  
**September 1, 2024**  
**ON SCHEDULE**






# Boyd & Green Elementary

Architect: Eley Guild Hardy  
Contractor: J.E. Stevens Construction  
Contract Amount: \$860,000  
Number of Contract Days: 220  
Number of Days into Construction: 98

## Project Scope

Window Replacements:  
New Windows West Elevation (Boyd)  
New Windows East Elevation (Green)

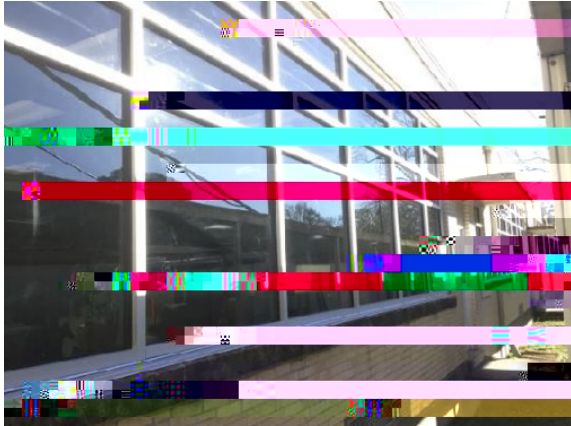


New Windows at Boyd  
Elementary



New Windows at Green  
Elementary

## Construction Completion

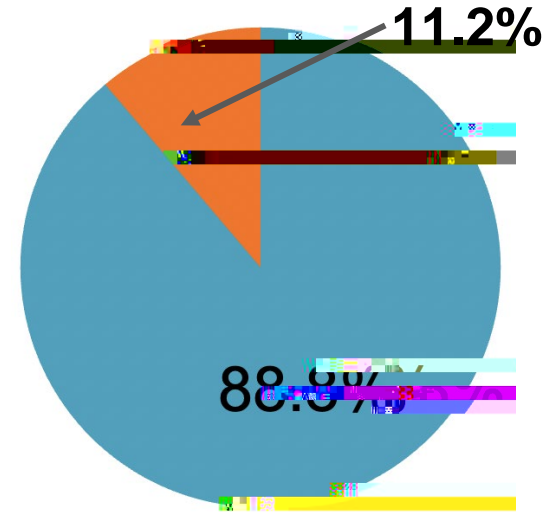

● COMPLETE ● INCOMPLETE

Contract Completion Date:

March 14, 2024

**ON SCHEDULE**



# John Hopkins Elementary

**Architect:** Allen Hoshall  
**Contractor:** M & P Construction  
**Contract Amount:** \$1,751,181  
**Number of Contract Days:** 200  
**Number of Days into Construction:** 170


## Project Scope

Girls' Restroom Renovations (8 Sets)  
Boys' Restroom Renovations (8 Sets)  
New VCT Flooring  
HVAC Upgrades



New HVAC Units Installed and Operable

## Construction Completion

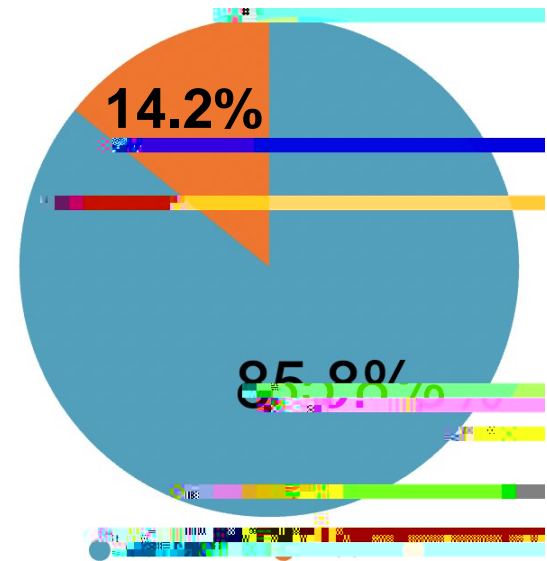


**Contract Completion Date:**  
**December 11, 2023**  
**SUBSTANTIALLY COMPLETE**  
**PENDING APPROVAL**






# McLeod Elementary

**Architect:** M3A Architecture  
**Contractor:** Mills Construction  
**Contract Amount:** \$907,800  
**Number of Contract Days:** 200  
**Number of Days into Construction:** 123

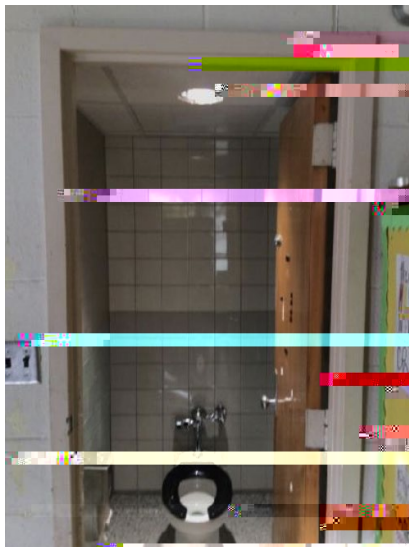


**Classroom #14 Restroom  
Complete**

**Project Scope**  
Plumbing Upgrades in Classrooms  
Gang and Staff Restroom Renovations  
New Millwork in Classrooms  
New Exterior Doors

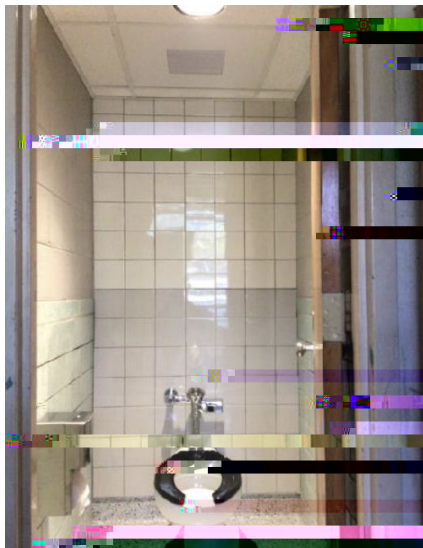

**Classroom #3 Restroom  
Complete**

## Construction Completion

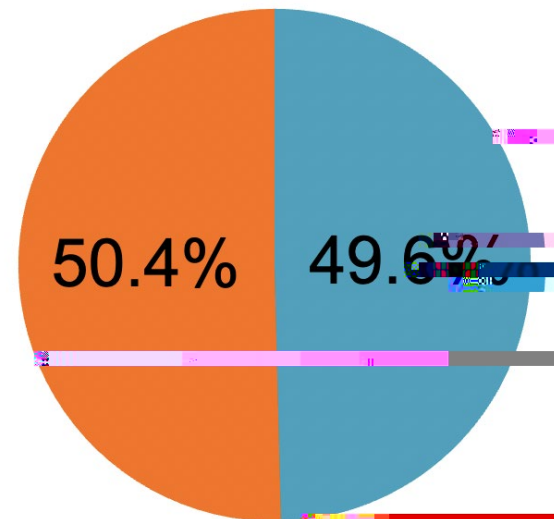

50.4% COMPLETE 49.6% REMAINING

**Contract Completion Date:**

**January 21, 2024**


**21 DAYS RECOMMENDED  
TIME EXTENSION**



# Pecan Park Elementary

## Project Scope

- New Facade & Replace Exterior Envelope
- HVAC Upgrades
- Restroom Renovations
- New Ceilings & Interior Lighting
- Structural Repairs & New Drainage System

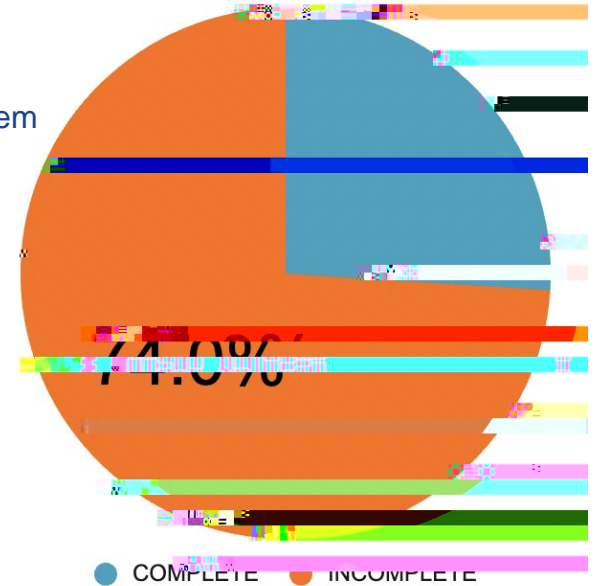

# Package B: Callaway, Kirksey, North Jackson, and McWillie HVAC Improvements

**Architect:** Canizaro Cawthon Davis  
**Contractor:** Upchurch Services  
**Contract Amount:** \$1,746,600  
**Number of Contract Days:** 400  
**Number of Days into Construction:** 22

**Project Scope**  
Indoor Air Quality Upgrades  
New HVAC Units


**Construction Start Date:**  
October 25, 2023  
**Contract Completion Date:**  
November 28, 2024  
**ON SCHEDULE**



Callaway High School



Kirksey Middle School



North Jackson Elementary  
School



McWillie Elementary  
School









  
**Jackson**  
PUBLIC SCHOOLS

**THANK YOU!**

