

LES Board Offices

Bond Construction Program - Phases II and III Design Team Selection

Facilities and Operations Staff and Vendors Bond Project Participation

Facilities and Operations Staff and Small Local Vendors:

Facilities and Operations staff and small contractors (vendors) have performed over 30 projects under \$50,000.00 via departmental work or informal bip formed

Elementary Schools

Boyd Elementary School (Remaining Corrective Work to be Completed)

1	Classrooms	speech room.
2	Classrooms	Code.

Van Winkle Elementary School (Completed)

Middle Schools

Bailey APAC Middle School (Remaining Corrective Work to be Completed)

1	Gymnasium
2	Classrooms
3	

2

High Schools

Callaway High School (Remaining Corrective Work to be Completed)

1	Classrooms	

Forest Hill High School (Remaining Corrective Work to be Completed)

High Schools

Jim Hill High School (Remaining Corrective Work to be Completed)

1 Gymnasium · Damaged bleachers.

Wingfield Hill High School (Remaining Corrective Work to be Completed)

1	Exterior	•	Water standing in the tunnel area under the school.				
2	Interior	•	Roof leaks throughout the buildings.				
3	Halls	•	Water enters the building under the East main hall exit door.				
4	Classrooms	•	No second means of egress in rooms 97, 98, 99, and 214.				
			(Note: All complete except room 214.)				
5	Classrooms	•	Roof leaks in rooms 97, 110, 112, and choir room.				
6	Classrooms	•	Water stands in the Northeast corner of room 110 after a big				
			rain.				

Major Projects Under Construction Spring and Summer 2020 Phase I (17 Locations)

School/Location	March	April	May	June	July	

Major Projects Under Construction Spring and Summer 2020 Phase I (17 Locations)

School/Location	March	April	May	June	July	August
Callaway High School - MDE						
Forest Hill High School - MDE						
Jim Hill High School - MDE						
Lanier High School						
Murrah High School						
Provine High School						


Major Projects Under Construction Spring and Summer 2020 Phase I (17 Locations)

Line Item Projects Under Construction Spring and Summer 2020 Phase II (18 Locations)


School/Location	March	April	May	June	July	August
Baker Elementary School						
Bates Elementary School						
John Hopkins Elementary School						
Johnson Elementary School						
Marshall Elementary School						
Oak Forest Elementary School						


Line Item Projects Under Construction Spring and Summer 2020 Phase II (18 Locations)







Chastain Middle School Portico and Walkway Repairs -



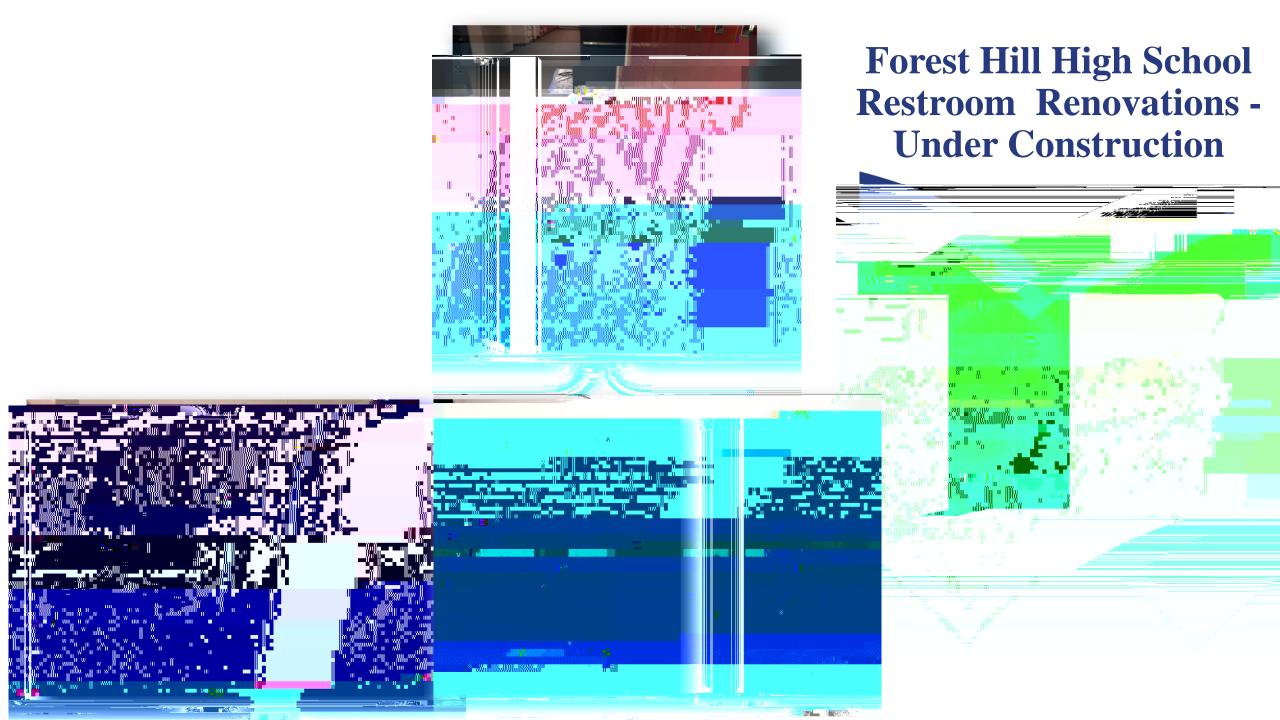





Thank You

We Welcome Any Questions
